PHASE 4: PROJECT PLANNING PHASE

EV Market Performance & Insights

Date	20 – October - 2026
Nasscom Student Id	SWUID2026399918
Project Name	Electric vehicle Market Performance & Insights

Project Planning Template

Purpose: This plan organizes the work required to deliver the Tableau EV market analysis, documentation, performance testing, and demonstration. Since the official blank Project Planning Template was not provided, the sections below use a standard project-planning structure; transfer the content into the trainer's template if its headings differ.

1. Project Overview

Project Name	EV Market Performance & Insights
Project Type	Data visualization and descriptive analysis
Primary Tool	Tableau (packaged workbook.twbx)
Data Assets	EV dataset files visible as ev_market_train and ev_market_test; confirm the exact file connected to the final workbook.
Core Deliverable	Interactive dashboard with 7 visualizations and a Tableau Story with 3 story points.
Supporting Deliverables	Business Question & Visualisation Report, Dashboard Design Template, Story Design Template, Performance Testing, final project documentation, demo video.
Project Scope	Explore EV category distribution, annual sales, manufacturer representation, battery technology, driving range, customer ratings, and manufacturing-country distribution.
Planning Basis	Indicative sequence; update dates and ownership to match the actual team plan.

2. Project Objectives


- Create a clear Tableau dashboard for the selected EV market questions.
- Use seven visualizations to compare the available EV measures and dimensions.
- Provide working filters for relevant dashboard fields.
- Arrange the analysis into three Tableau Story points.
- Verify chart values, labels, filter behavior, and navigation before submission.
- Prepare complete project documentation, supporting PDFs, and a demonstration video.

3. Work Breakdown Structure (WBS)

WBS ID	Activity / Task	Expected Output	Status (update)
1.0	Confirm scope and business questions	Final question list	Completed / verify
2.0	Review dataset and Tableau data connection	Confirmed data source and field list	Completed / verify
3.0	Create category, sales, manufacturer, battery, range, rating, and country views	7 Tableau visualizations	Dashboard visible; verify final workbook
4.0	Assemble dashboard and configure filters	Interactive dashboard	Dashboard visible; test filters
5.0	Arrange Story points	3-point Tableau Story	Story navigation visible; verify
6.0	Test data accuracy, filters, readability, and navigation	Performance Testing evidence	In progress / verify
7.0	Prepare phase documents and screenshots	Required documentation files	Several files visible; verify completeness
8.0	Record and review project demonstration	Demo video	Not visible in latest file screenshot
9.0	Export and organize final submission files	PDFs and final folder structure	Pending final review

4. Project Schedule / Timeline

The timeline below is an indicative 8-day working sequence, not a claim about the actual dates spent. Since the dashboard and several documents already exist, mark completed activities accordingly and adjust the remaining schedule to the submission deadline.

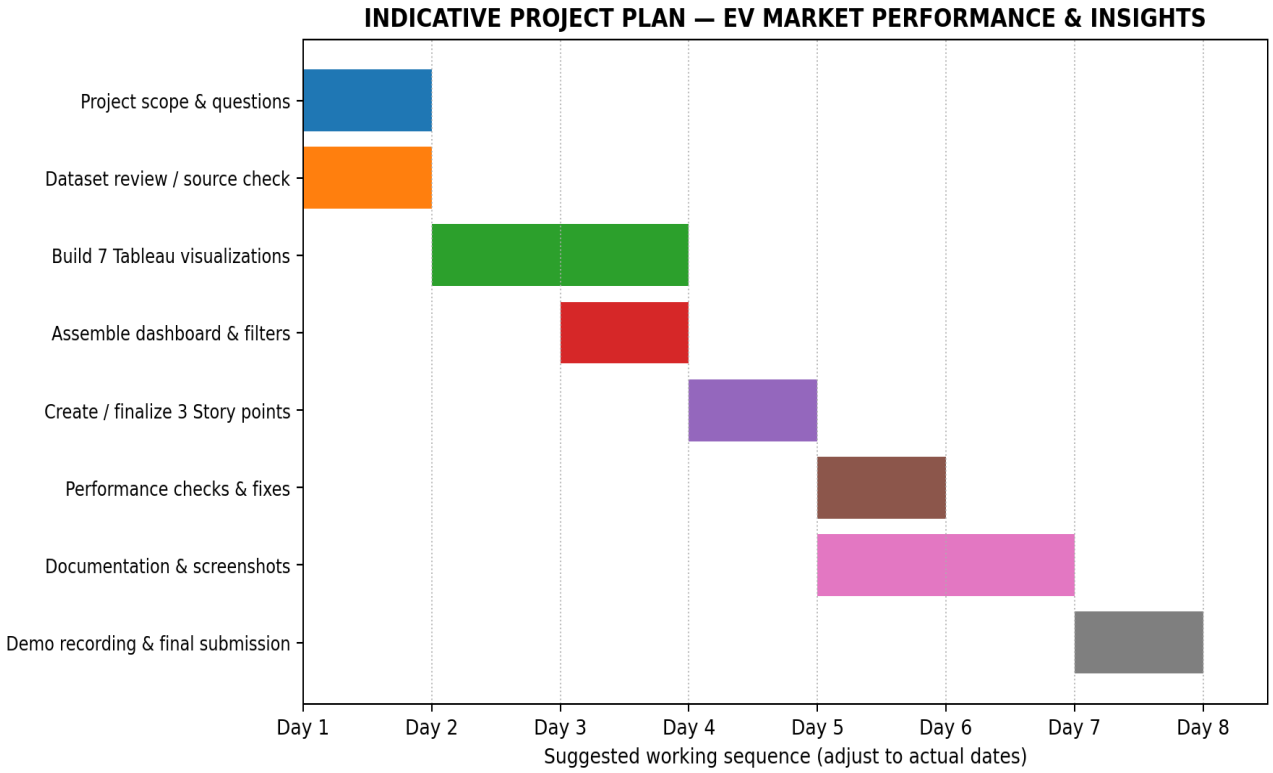

Suggested Time	Main Activity	Milestone
Day 1	Confirm scope, data source, and chart questions	Scope confirmed
Day 2	Review fields and complete any required data checks	Data source verified
Days 3–4	Finalize seven visualizations, dashboard layout, and filters	Dashboard ready
Day 5	Verify the three Story points and narrative	Story ready
Day 6	Test filters, values, labels, navigation, and screen readability	Testing reviewed
Days 6–7	Complete phase documents and capture screenshots	Documentation ready
Day 8	Record demo, export PDFs, and check final folder	Submission package ready

5. Roles and Responsibilities

Use the following responsibility table for an individual or team project. Replace role labels with actual team member names only if required by the official template.

Role	Responsibility	Owner
Project Coordinator	Track scope, deliverables, and submission checklist.	Project team / student
Data & Tableau Analyst	Check data source, build charts, configure filters, and verify values.	Project team / student
Documentation Lead	Prepare reports, screenshots, and phase-wise documents.	Project team / student
Testing & Demo Lead	Test dashboard behavior and record the demonstration.	Project team / student

6. Resources Required

- EV dataset file(s) used by the final workbook.
- Tableau Desktop or Tableau Public environment used to create/open the packaged workbook.
- Computer capable of opening the Tableau workbook and capturing screenshots.
- Microsoft Word or compatible editor for documentation and PDF export.
- Screen recording tool for the demonstration video.
- Official NASSCOM templates and submission instructions.

7. Risks and Mitigation Plan


Risk	Possible Impact	Mitigation
Wrong or unclear data source	Charts may not match the intended dataset.	Open the final workbook and confirm its data source and field names.
Overlapping labels / crowded layout	Dashboard becomes difficult to read.	Resize charts, simplify labels, sort bars, and retest at normal screen size.
Filters not applying as expected	Users may draw incorrect comparisons.	Test each filter and confirm which worksheets it affects.
Unsupported findings	Report may overstate what the data shows.	Verify claims against chart values and source data.
Missing submission documents	Incomplete project package.	Use the phase checklist and review

		the final folder.
Demo recording issues	Features may not be visible or audio may be unclear.	Run a short test recording before the final capture.

8. Milestones and Deliverables

Milestone	Evidence / Deliverable	Completion Check
M1 — Scope approved	Problem statement and business questions	Questions align with seven charts.
M2 — Dashboard built	Tableau packaged workbook	All seven charts visible and relevant.
M3 — Story ready	Tableau Story	Three points open and tell a coherent sequence.
M4 — Testing reviewed	Performance Testing document	Required parameters and evidence filled.
M5 — Documentation ready	Phase documents and final project report	Headings match official templates; screenshots readable.
M6 — Demo ready	Demo video	Dashboard, filters, and Story demonstrated.
M7 — Submission packaged	PDFs, workbook, and required links/files	All required items present in the correct folders.

9. Project Workflow

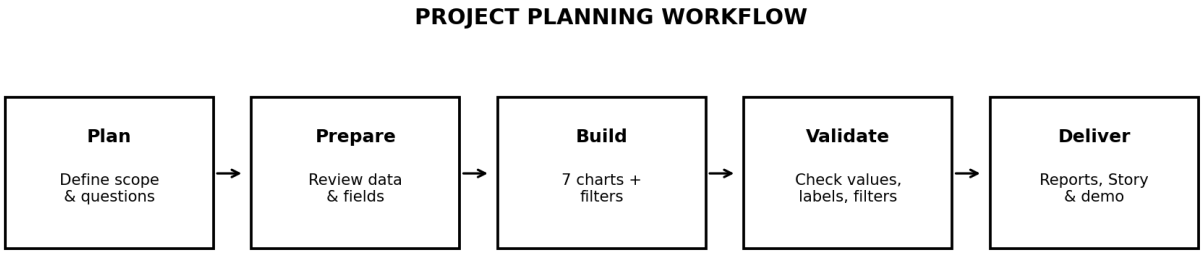

Use this sequence as a plan; mark each activity complete only after checking the actual deliverable.
